NATIONAL CANCER CONTROL PROGRAM - GEORGIA
UPGRADING OF NATIONAL CANCER INSTITUTE
PROJECT ROAD MAP FOR IMPLEMENTATION

Duration in MONTH from project start
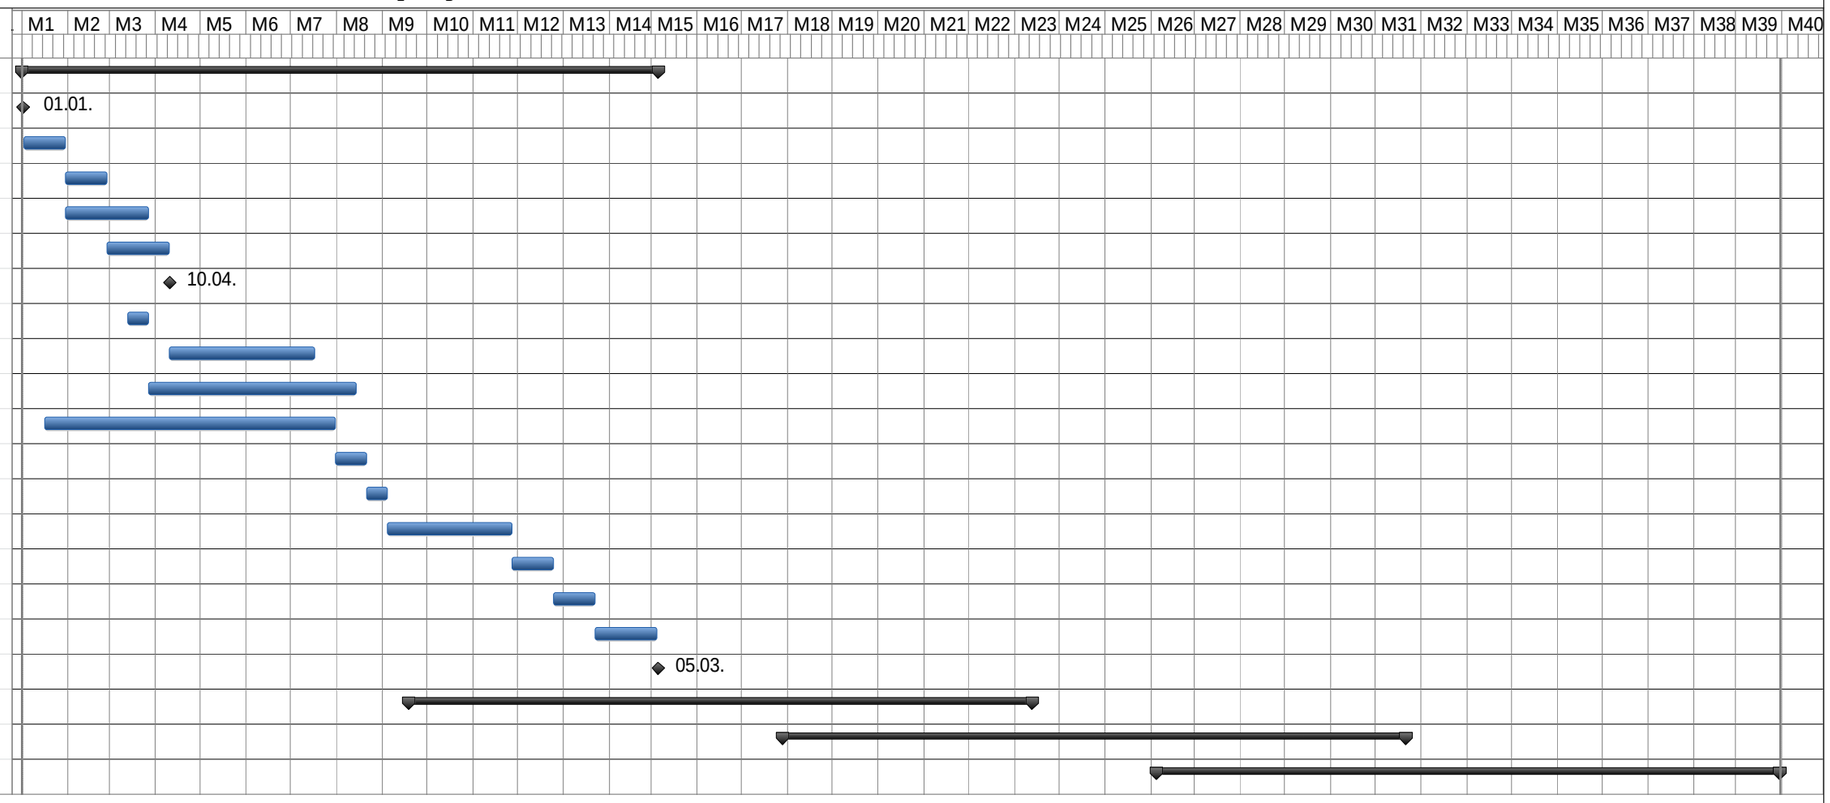
Nr.	Vorgangsname	Dauer days
1	Phase 1	307 Tage?
2	Contract effective date	1 Tag
3	Evalustion as built	20 Tage
4	Master plan phases	20 Tage
5	Engineering phase 1	40 Tage
6	Authority approvals	30 Tage
7	Project approved	1 Tag?
8	Site mobilisation	10 Tage
9	Construction bunker	70 Tage
10	Renovation existing building areas	100 Tage
11	Procurement of equipment	140 Tage
12	Shipment	15 Tage
13	Custom clearance	10 Tage
14	Assembling Installation	60 Tage
15	Testing	20 Tage
16	Comissioning Safety tests	20 Tage
17	Training phase	30 Tage
18	Regular operation with patients	1 Tag
19	Phase 2	300 Tage
20	Phase 3	300 Tage
21	Phase 4	300 Tage
